West Chester University Campus Master Plan Update Final Draft

CMP PROJECT OPPORTUNITIES

HOUSING

- Lawrence Hall Demo & Build New Housing
- College Arms Apartments Renovations
- South Campus Apartments –Full Reno w/ Vertical Expansion
- Tyson Hall Full Reno w/ Addition
- Goshen Hall Full Reno w/ Addition
- Killinger Hall Demo & Build New Housing
- Schmidt Hall Full Reno w/ Entry Addition

ACADEMIC

- Science Center Complex Renovation
- Old Library Renovation
- FHG Library Renovation
- Sturzebecker Renovation
- EO Bull Center for the Arts Expansion & Landscape Improvements

STUDENT SERVICES

- Improve or Build New South Campus Commons Building
- Expand Sykes for Student Services, Welcome Center, Dining, and Parking

CAMPUS IMPROVEMENTS

- Church St & University Ave Improvements
- Rosedale Ave Improvements
- Ram Park Relocation
- Land Acquisition to complete "superblock"
- New St and Rosedale Recreation Addition
- Improved gateway at New St across from Sturzebecker and athletic fields
- Improvements at Farrell Stadium
- Athletic field amenities (restrooms, concessions, etc)
- President's Walk Extension
- Planning Study for Tanglewood Residence & Grounds (highest and best use of property)


CAMPUS SUPPORT


- 210 & 220 East Rosedale
- Maintenance Garage
- 201 Carter Utilization
- 204 Carter vacant
- Alumni & Foundation Center
- 887 Matlack relocate public safety

CAMPUS IMPROVEMENT PROGRAMS -SUSTAINABILITY

- Existing Geothermal Deferred Maintenance
- New St multimodal campus connector
- Gordon Preserve Connections
- Bike-share program



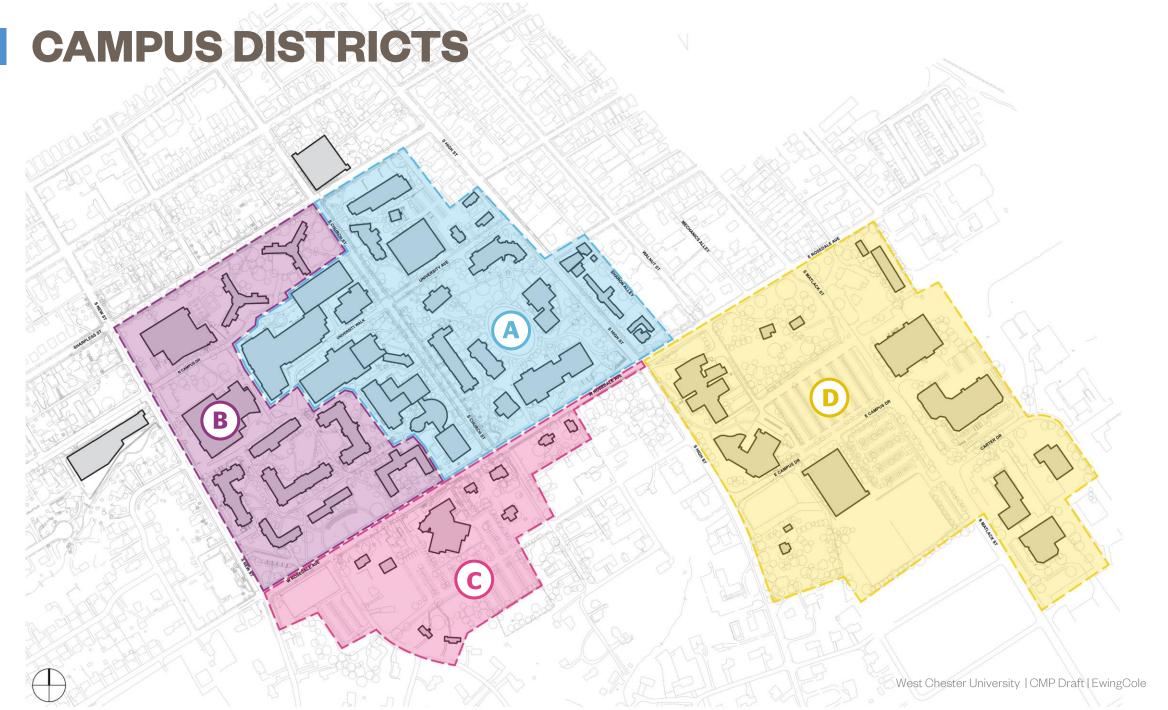

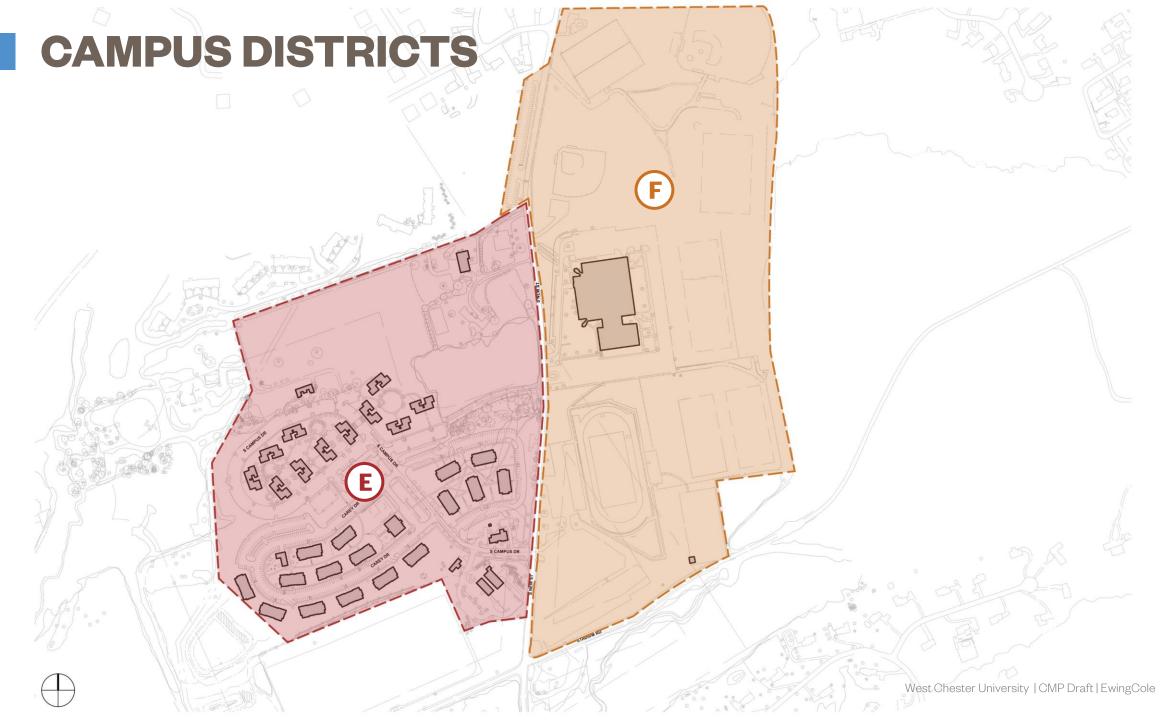

0-5 YEARS


- 1. Science Center Complex Renovation
- 2. Old Library Renovation
- 3. FHG Library Renovation
- 4. College Arms Apartments Renovation

6-10 YEARS

5. Church Street & University Ave Improvements

10+YEARS

6. Land acquisition to complete "superblock" (Corner of Sharpless & S High St)

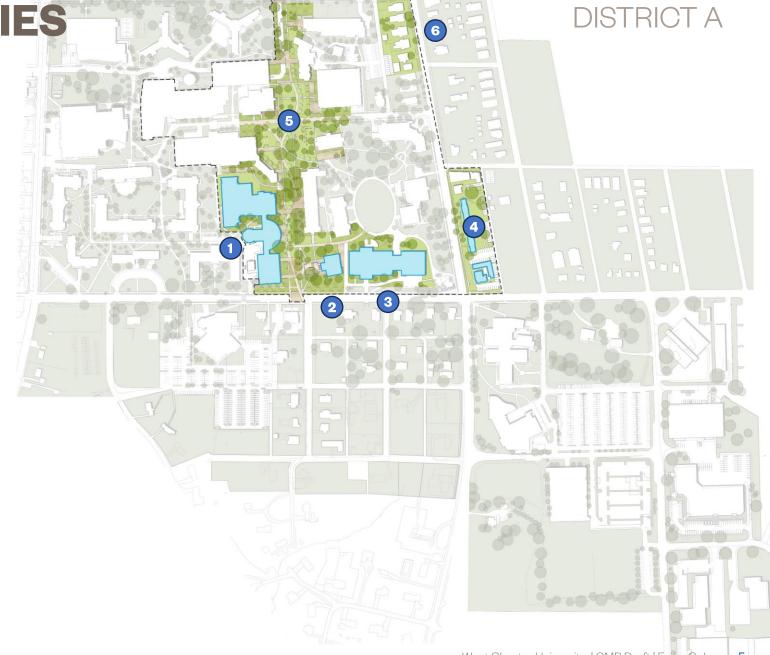

DISTRICT B

0-5 YEARS


- Lawrence Hall Demo & Build New Housing
- Existing Geothermal Deferred Maintenance

6-10 YEARS

- Tyson Hall Full Reno w/ Addition
- Goshen Hall Full Reno w/ Addition

10+ YEARS

- Killinger Hall Demo & Build New Housing
- Schmidt Hall Full Reno w/ New Entry Addition

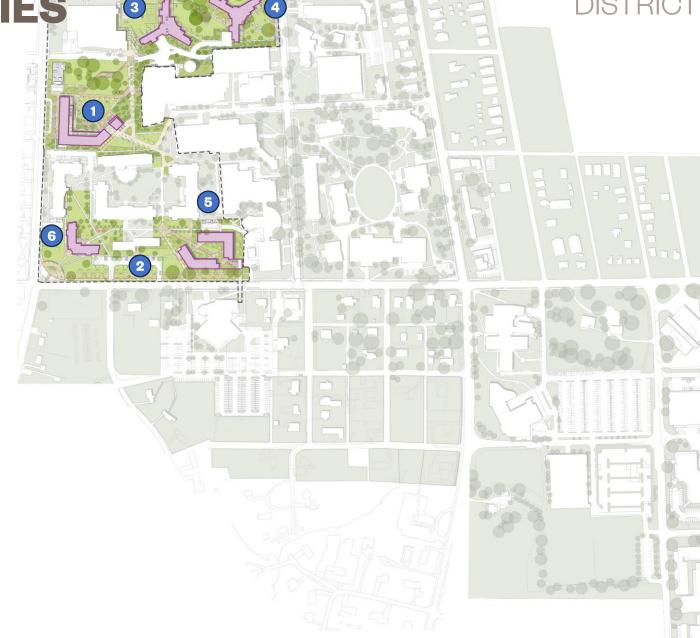

DISTRICT C

0-5 YEARS


- Sykes Student Union Expansion (Student Services, Dining, & Welcome Center)
- Rosedale Ave Improvements
- Existing Geothermal Deferred Maintenance

6-10 YEARS

Ram Park Relocation (Across Church St)

10+YEARS

- Sykes Student Union Parking Deck
- Recreation Improvements (corner of Rosedale Ave & New St)

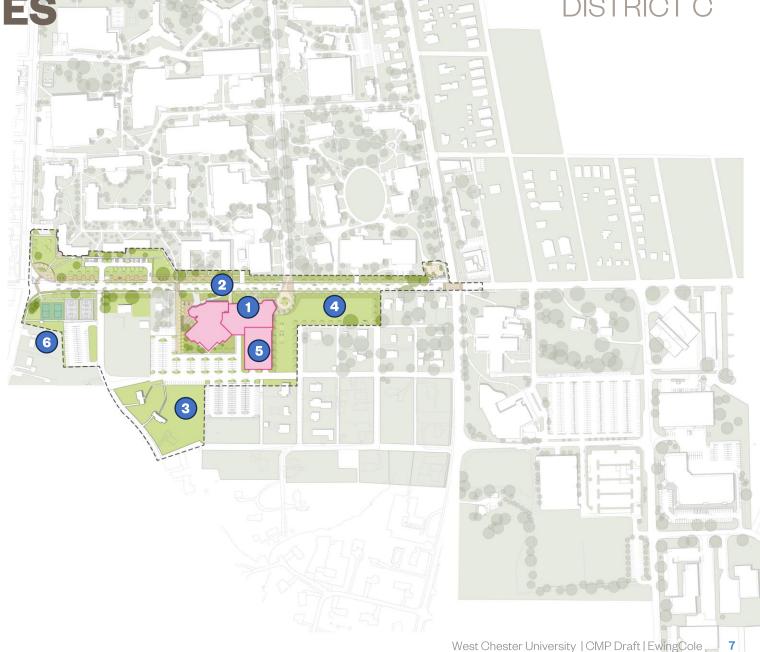

0-5 YEARS


- 1. Temporary Housing
- 2. Removal of temporary housing & reinstate M1 Lot as parking

6-10 YEARS

10+YEARS

- 2. EO Bull Center for the Arts Expansion & Landscape Improvements
- 3. Planning Study for Tanglewood Residence & Grounds (highest and best use of property)
- 4. President's Walk Extension (Landscape)

*Campus Support Projects can be implemented at any time.

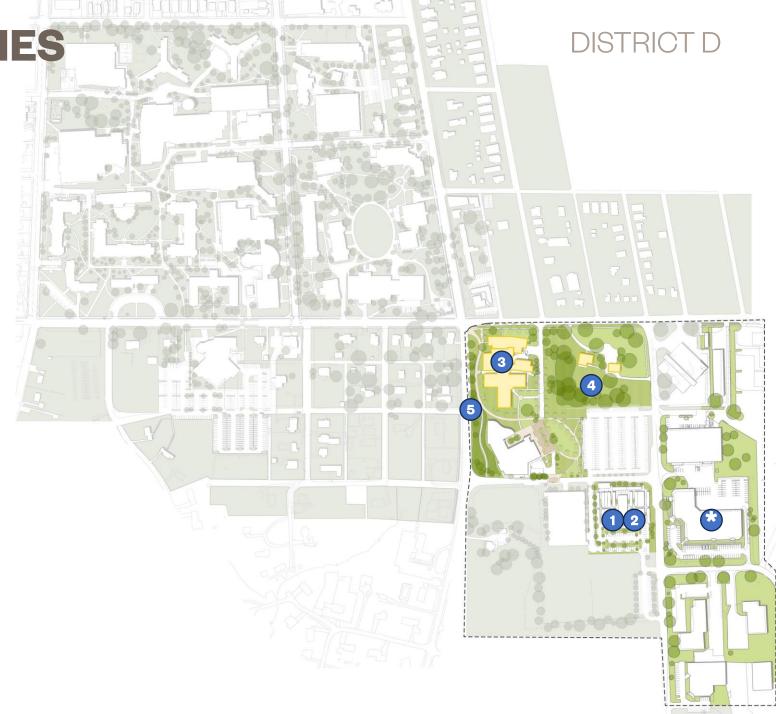


0-5 YEARS

- South Campus Apartments Full Reno w/Vertical Expansion
- 2. Improve or Build New South Campus Commons Building (location to be determined)

6-10 YEARS

3. South Campus Gateway connection to Sturzebecker and athletic fields

10+ YEARS

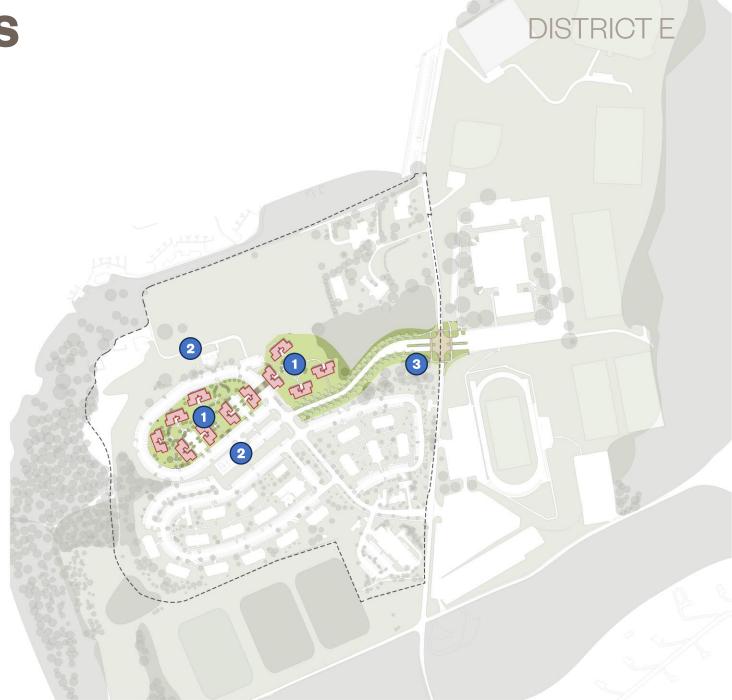

0-5 YEARS

1. Sturzebecker Renovation

6-10 YEARS

- 2. Farrell Stadium Improvements
- 3. Athletic field amenities (restrooms, concessions, etc)

10+YEARS

- 4. Gordon Preserve Trail Connections
- 5. New St Multi-Modal Transportation





PROJECT PRIORITIZATION

2025	2030	2031	2035	2035
0-5 YEAR	S I	6-10	YEARS I	10+ YEARS
Science Center Co Old Library Renova FHG Library Renova Lawrence Hall – De Housing Existing Geotherm Maintenance Sykes Student Unio Services, Dining, & Rosedale Ave Impr Temporary Housin Removal of temporary reinstate M1 Lot as	ation vation emo & Build New al Deferred on Expansion (Student Welcome Center) rovements g rary housing & parking artments – Full Reno on ew South Campus	 Tyson Hall – Full Goshen Hall – Full Ram Park Reloct South Campus Gouth Sturzebecker ar Farrell Stadium 	Il Reno w/ Addition full Reno w/ Addition cation (Across Church St) Gateway connection to and athletic fields Improvements anenities (restrooms, concessions,	 Land acquisition to complete "superblock" (Corner of Sharpless & S High St) Killinger Hall – Demo & Build New Housing Schmidt Hall – Full Reno w/ New Entry Addition Sykes Student Union Parking Deck Recreation Improvements (corner of Rosedale Ave & New St) EO Bull Center for the Arts Expansion & Landscape Improvements Planning Study for Tanglewood Residence & Grounds (highest and best use of property) President's Walk Extension (Landscape) Gordon Preserve Trail Connections New St Multi-Modal Transportation

STUDENT HOUSING PROJECT PRIORITIZATION

HOUSING IMPLEMENTATION TIMELINE		Year	1	,	Year 2		Yea	ar 3	Y	ear 4		Year	5	Ye	ar 6		Yea	r 7		Year 8	8	١	ear 9		Year	10		Year:	11	Υ	ear 12	2	Ye	ar 13	3	Yea	ar 14		Year	15
Academic Calander Year (Summer - Fall - Spring)	Summer 2025	Fall 2025	Spring 2026	Summer 2026	Fall 2026	Spring 2027	Summer 2027	Spring 2028	Summer 2028	Fall 2028	Spring 2029	Fall 2029	Spring 2030	Summer 2030	Fall 2030 Spring 2031	Summer 2031	Fall 2031	Spring 2032	Summer 2032	Fall 2032	Spring 2033	Summer 2033	Fall 2033	Spring 2034	Summer 2034	Spring 2035	Summer 2035	Fall 2035	Spring 2036	Summer 2036	Fall 2036	Spring 2037	Summer 2037	Fall 2037	Spring 2038	Summer 2038	Fall 2038	Summer 2039	Fall 2039	Spring 2040
			_																																					
			<u>/</u>	A				odulars				ration		st Cam	ipus)	4																								
Temporary Modular Housing Units					— Ма	ах Ос	cupan	cy Dui	ration				>																											
Start South Campus Apartments Phase 1		(1		Start	SCA F	hase	1																																
Occupy Phase 1		V	/								7																													
occupy Filase 1							Fi	nish SC	A- Ph	ase 1																														
Start South Campus Apartments Phase 2										\neq	SCA	A- Pha	se 2																											
Occupy Phase 2									•																															
																la	wren	re Ha	all																					
Start Lawrence Hall Demo + Construction				De	emo											Lu	2001 C11		u.,																					
Occupy Lawrence														•																										
Start South Campus Apartments Phase 3									•					SCA- P	hase 3	3																								
Occupy Phase 3											•	•				Ŧ																								
Start South Campus Apartments Phase 4												•							SCA	۱- Pha	se 4																			
Occupy Phase 4																	•																							
Start Tyson Hall Renovation														•								Tysor	n Hall	\dashv																
Occupy Tyson																			•																					
Start Goshen Hall Renovation																									+		Soshe	en Ha	II											
Occupy Goshen																								•																
Start Killinger Hall Demo + Construction																																		$\overline{}$	Killi	inger I	Hall			
Occupy Killinger																						De	mo										•					-		
-																																			Schr	midt I	1811			
Start Schmidt Hall Renovation + Addition																																								
Occupy Schmidt																																								
